Is it final bill

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

67318

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work:- Construction & Repairs to Culverts in Dasarahalli in ward No-15						
	Estimate cost:- RS 20.00 lakhs.						
	Job code:- 015-18-000027 P-code:- 1771						
	D.O No:- EE/DD/NO/272/17-18. Dt. 12/3/18.						
	A.A. No:- EE/DD/AS/564/17-18, Dt. 29/11/17.						
	T.S No:- EE/DZ/TS/399/17-18, Dt. 30/11/17.						
	Tender Notification No:- BBMP/EE/DD/TEN/05/17-18, Dt. 04/12/17.						
	Agency:- Sri. D.V. Kumar.						
	Inclination:- 05/09/18						

Scanned by CamScanner

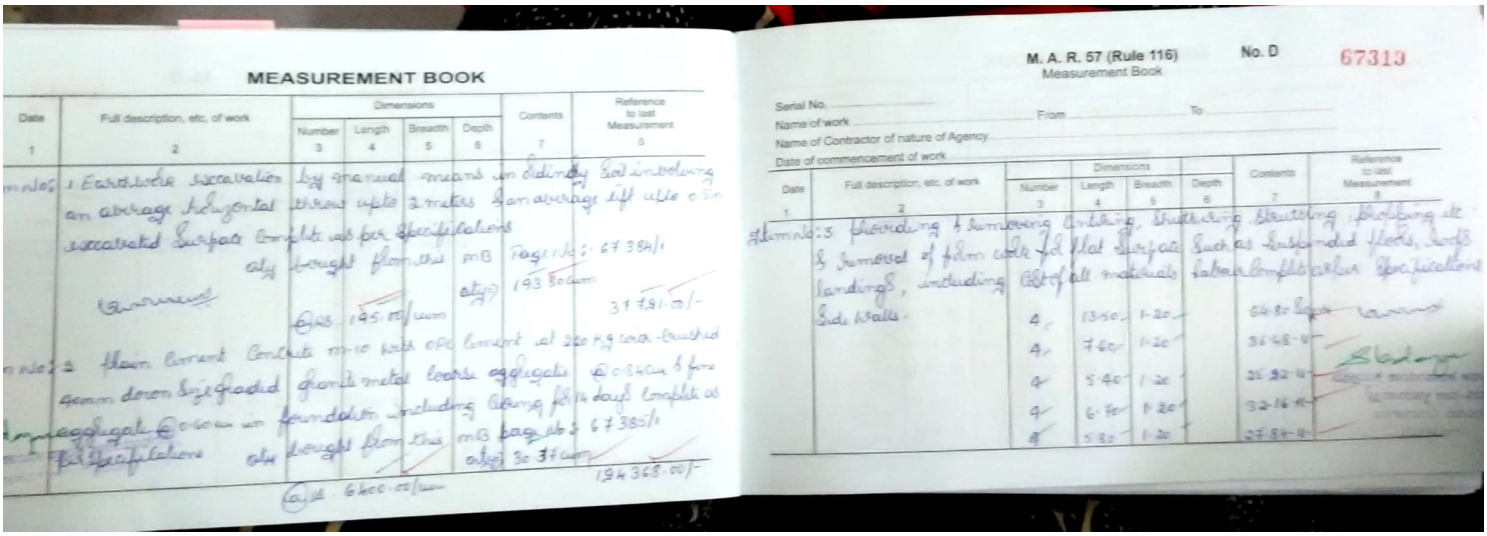

MEASUREMENT BOOK

Date	Full description, etc. of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	1 Earthwork excavation by manual means in ordinary Soil involving an average horizontal throw upto 2 meters & an average lift upto 0.5m excavated Surface Complete as per Specifications						
	qty brought from this page					Page No: 67384/1	
	Extra					193.80 cum	
	Extra 195.00/cum					37781.00/-	
	2 Plain Cement Concrete m-10 with OPC Cement at 220 kg/cum Crushed granite metal Coarse aggregate @ 0.84 cum & fine aggregate @ 0.42 cum in foundation including Curing for 14 days Complete as per Specifications						
	qty brought from this page					Page No: 67385/1	
	Extra 6400.00/cum					30.37 cum	
						194368.00/-	

M. A. R. 57 (Rule 116) No. D 67313
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor or nature of Agency .....
Date of commencement of work .....

Date	Full description, etc. of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Providing & Lowering Centering, Shuttering, Stretching, Propping etc & removal of form work for flat Surface such as Suspended floors, roofs landings, including cost of all materials labour Complete as per Specifications						
	Side walls.	4	13.50	1.20		64.80 Sqm	
		4	7.60	1.20		36.48	
		4	5.40	1.20		25.92	
		4	6.70	1.20		32.16	
		4	5.80	1.20		27.84	

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		4	7.90	1.20		37.92-11	
		4	5.60	1.20		26.88-11	
		4	6.00	1.20		28.80-11	
		4	4.80	1.00		19.20-11	
	Td Slab	1	13.50	3.50		47.25-11	
		1	7.60	2.60		19.76-11	
		1	5.40	2.30		12.42-11	
		1	6.70	2.30		15.41-11	
		1	5.80	2.30		13.34-11	
		1	7.90	2.30		18.17-11	

M. A. R. 57 (Rule 116) No. D 67320

Measurement Book

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		1	5.60	2.60		14.56-11	
		1	6.00	2.30		13.80-11	
		1	4.80	2.00		9.60-11	
						⇒ 464.31 Sqm	
				Amended	Lo ⇒	460.80 Sqm	
		@ RS.	407.00/Sqm				187546.00/-
	Item No 4 Design mix M30 with OPC cement @ 320 Kgs with 20mm & down size graded granite metal coarse aggregate & 0.69 cm on fine aggregate						

Scanned by CamScanner

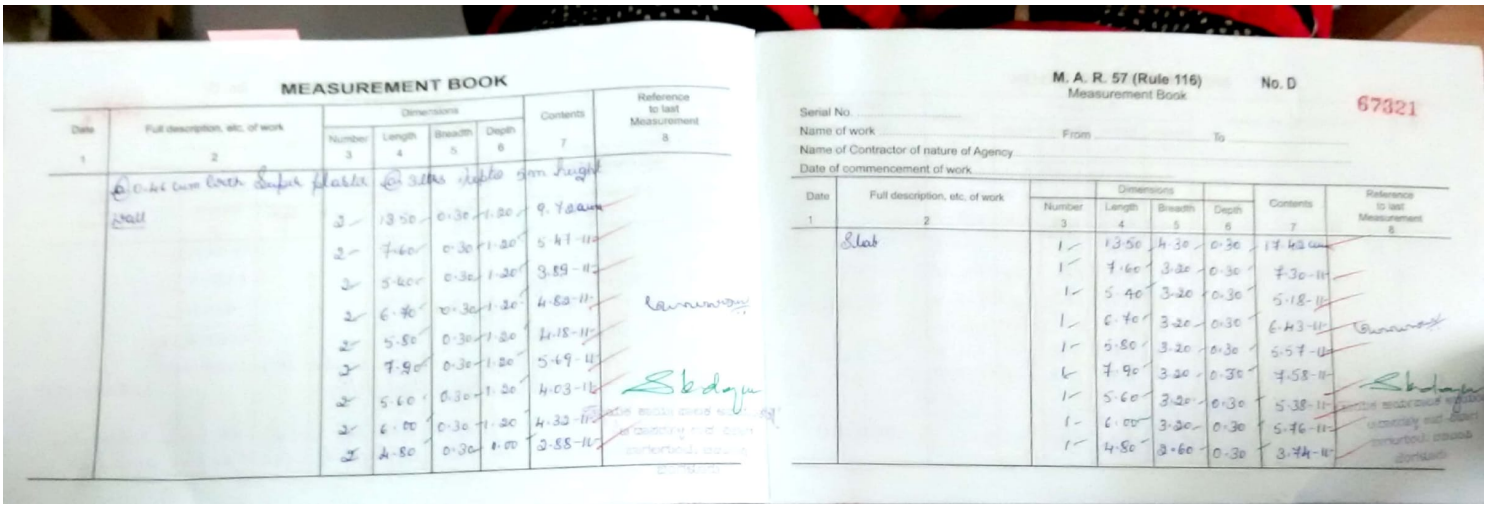

MEASUREMENT BOOK

Date	Full description, etc. of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	@ 0.46 cum Each Super plastic @ 3 hrs ratio 5cm height wall	2	13.50	0.30	1.20	9.72 cum	
		2	7.60	0.30	1.20	5.47-11	
		2	5.40	0.30	1.20	3.89-11	
		2	6.70	0.30	1.20	4.82-11	
		2	5.80	0.30	1.20	4.18-11	
		2	7.90	0.30	1.20	5.69-11	
		2	5.60	0.30	1.20	4.03-11	
		2	6.00	0.30	1.20	4.32-11	
		2	4.80	0.30	1.00	2.88-11	

M. A. R. 57 (Rule 116) No. D

Measurement Book

67321

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc. of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Slab	1	13.50	4.30	0.30	17.42 cum	
		1	7.60	3.20	0.30	7.30-11	
		1	5.40	3.20	0.30	5.18-11	
		1	6.70	3.20	0.30	6.43-11	
		1	5.80	3.20	0.30	5.57-11	
		6	7.90	3.20	0.30	4.58-11	
		1	5.60	3.20	0.30	5.38-11	
		1	6.00	3.20	0.30	5.76-11	
		1	4.80	3.60	0.30	3.74-11	

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Bottom cord	1	13.50	1.50	0.20	4.05	
		1	7.60	1.00	0.20	1.52	
		1	5.40	1.00	0.20	1.08	
		1	6.70	1.00	0.20	1.34	
		1	5.80	1.00	0.20	1.16	
		1	7.90	1.00	0.20	1.58	
		1	5.60	1.00	0.20	1.12	
		1	6.00	1.00	0.20	1.20	
		1	4.80	1.00	0.20	0.96	
						123.37 cum	
		@ Rs 7200.00/cum					888.264.00/-

M. A. R. 57 (Rule 116) No. D

Measurement Book

67322

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Item No: 5 Supplying, fitting & placing TMT bar reinforcement in Sub-Structure Complete as per drawing & technical Specifications						Complete as per Specifications
	qty brought from this MB page No: 67386/1					10.860.96 Kg	
					qty =	10.860 tonne	
		@ Rs 61600.00/tonne					668976.00/-
	Item No: 6 Disposal of debris to the final place of disposal with all lead & lift & as direction by the engineer in charge of the work, lead, 4Km c) add loading & unloading.						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		Qty vide Item No-1					
					Qty =	193.80 cum	
		@ Rs	85.00/cum				16473.00/-
					Total bill amt =		1993418.00/-
	Conclusion						

Certificate:-

1) This is to Certify that the Contractor has Completed the work Satisfactorily

2) The Contractor has cleared the debris from the work Site

3) There are no departmental issues for the above work.

Sudagar

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶ್ರೀ ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಜಿಕೆವಿಕೆ
ಬೆಂಗಳೂರು

Scanned by CamScanner
